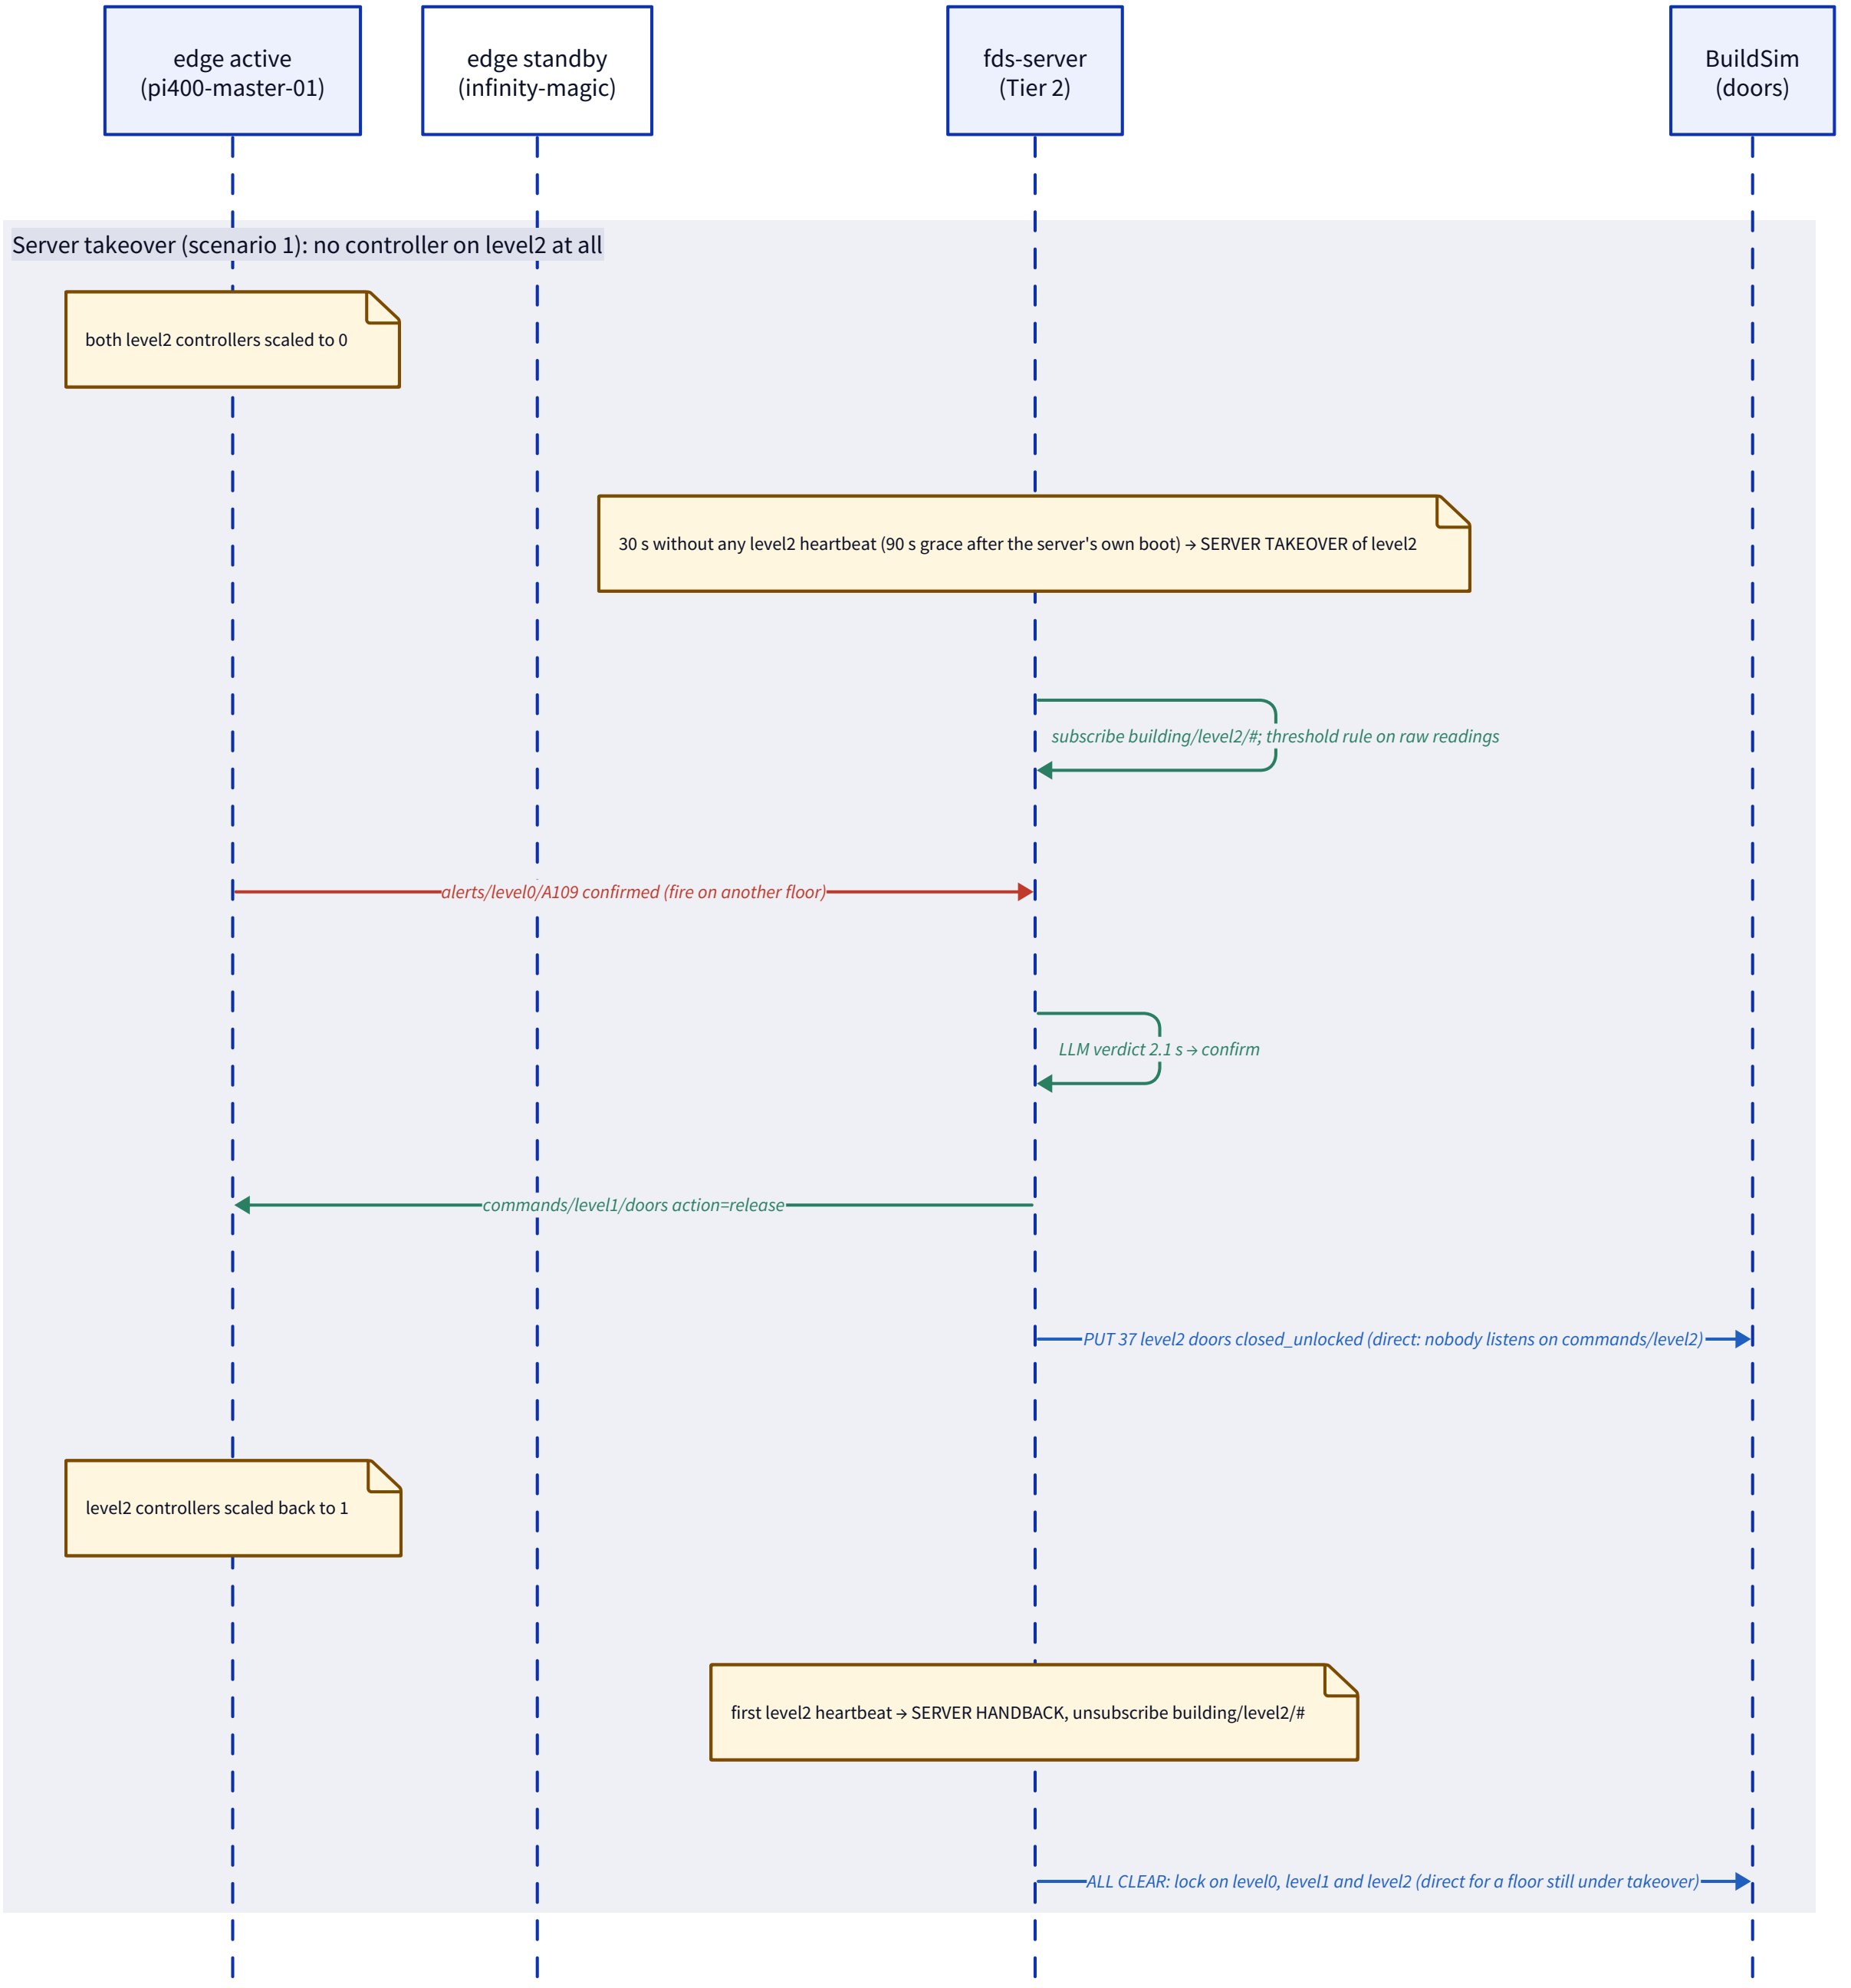

edge active
(pi400-master-01)
edge standby
(infinity-magic)
fds-server
(Tier 2)
BuildSim
(doors)
Server takeover (scenario 1): no controller on level2 at all
both level2 controllers scaled to 0
30 s without any level2 heartbeat (90 s grace after the server's own boot) → SERVER TAKEOVER of level2
subscribe building/level2/#; threshold rule on raw readings
alerts/level0/A109 confirmed (fire on another floor)
LLM verdict 2.1 s → confirm
commands/level1/doors action=release
PUT 37 level2 doors closed_unlocked (direct: nobody listens on commands/level2)
level2 controllers scaled back to 1
first level2 heartbeat → SERVER HANDBACK, unsubscribe building/level2/#
ALL CLEAR: lock on level0, level1 and level2 (direct for a floor still under takeover)
