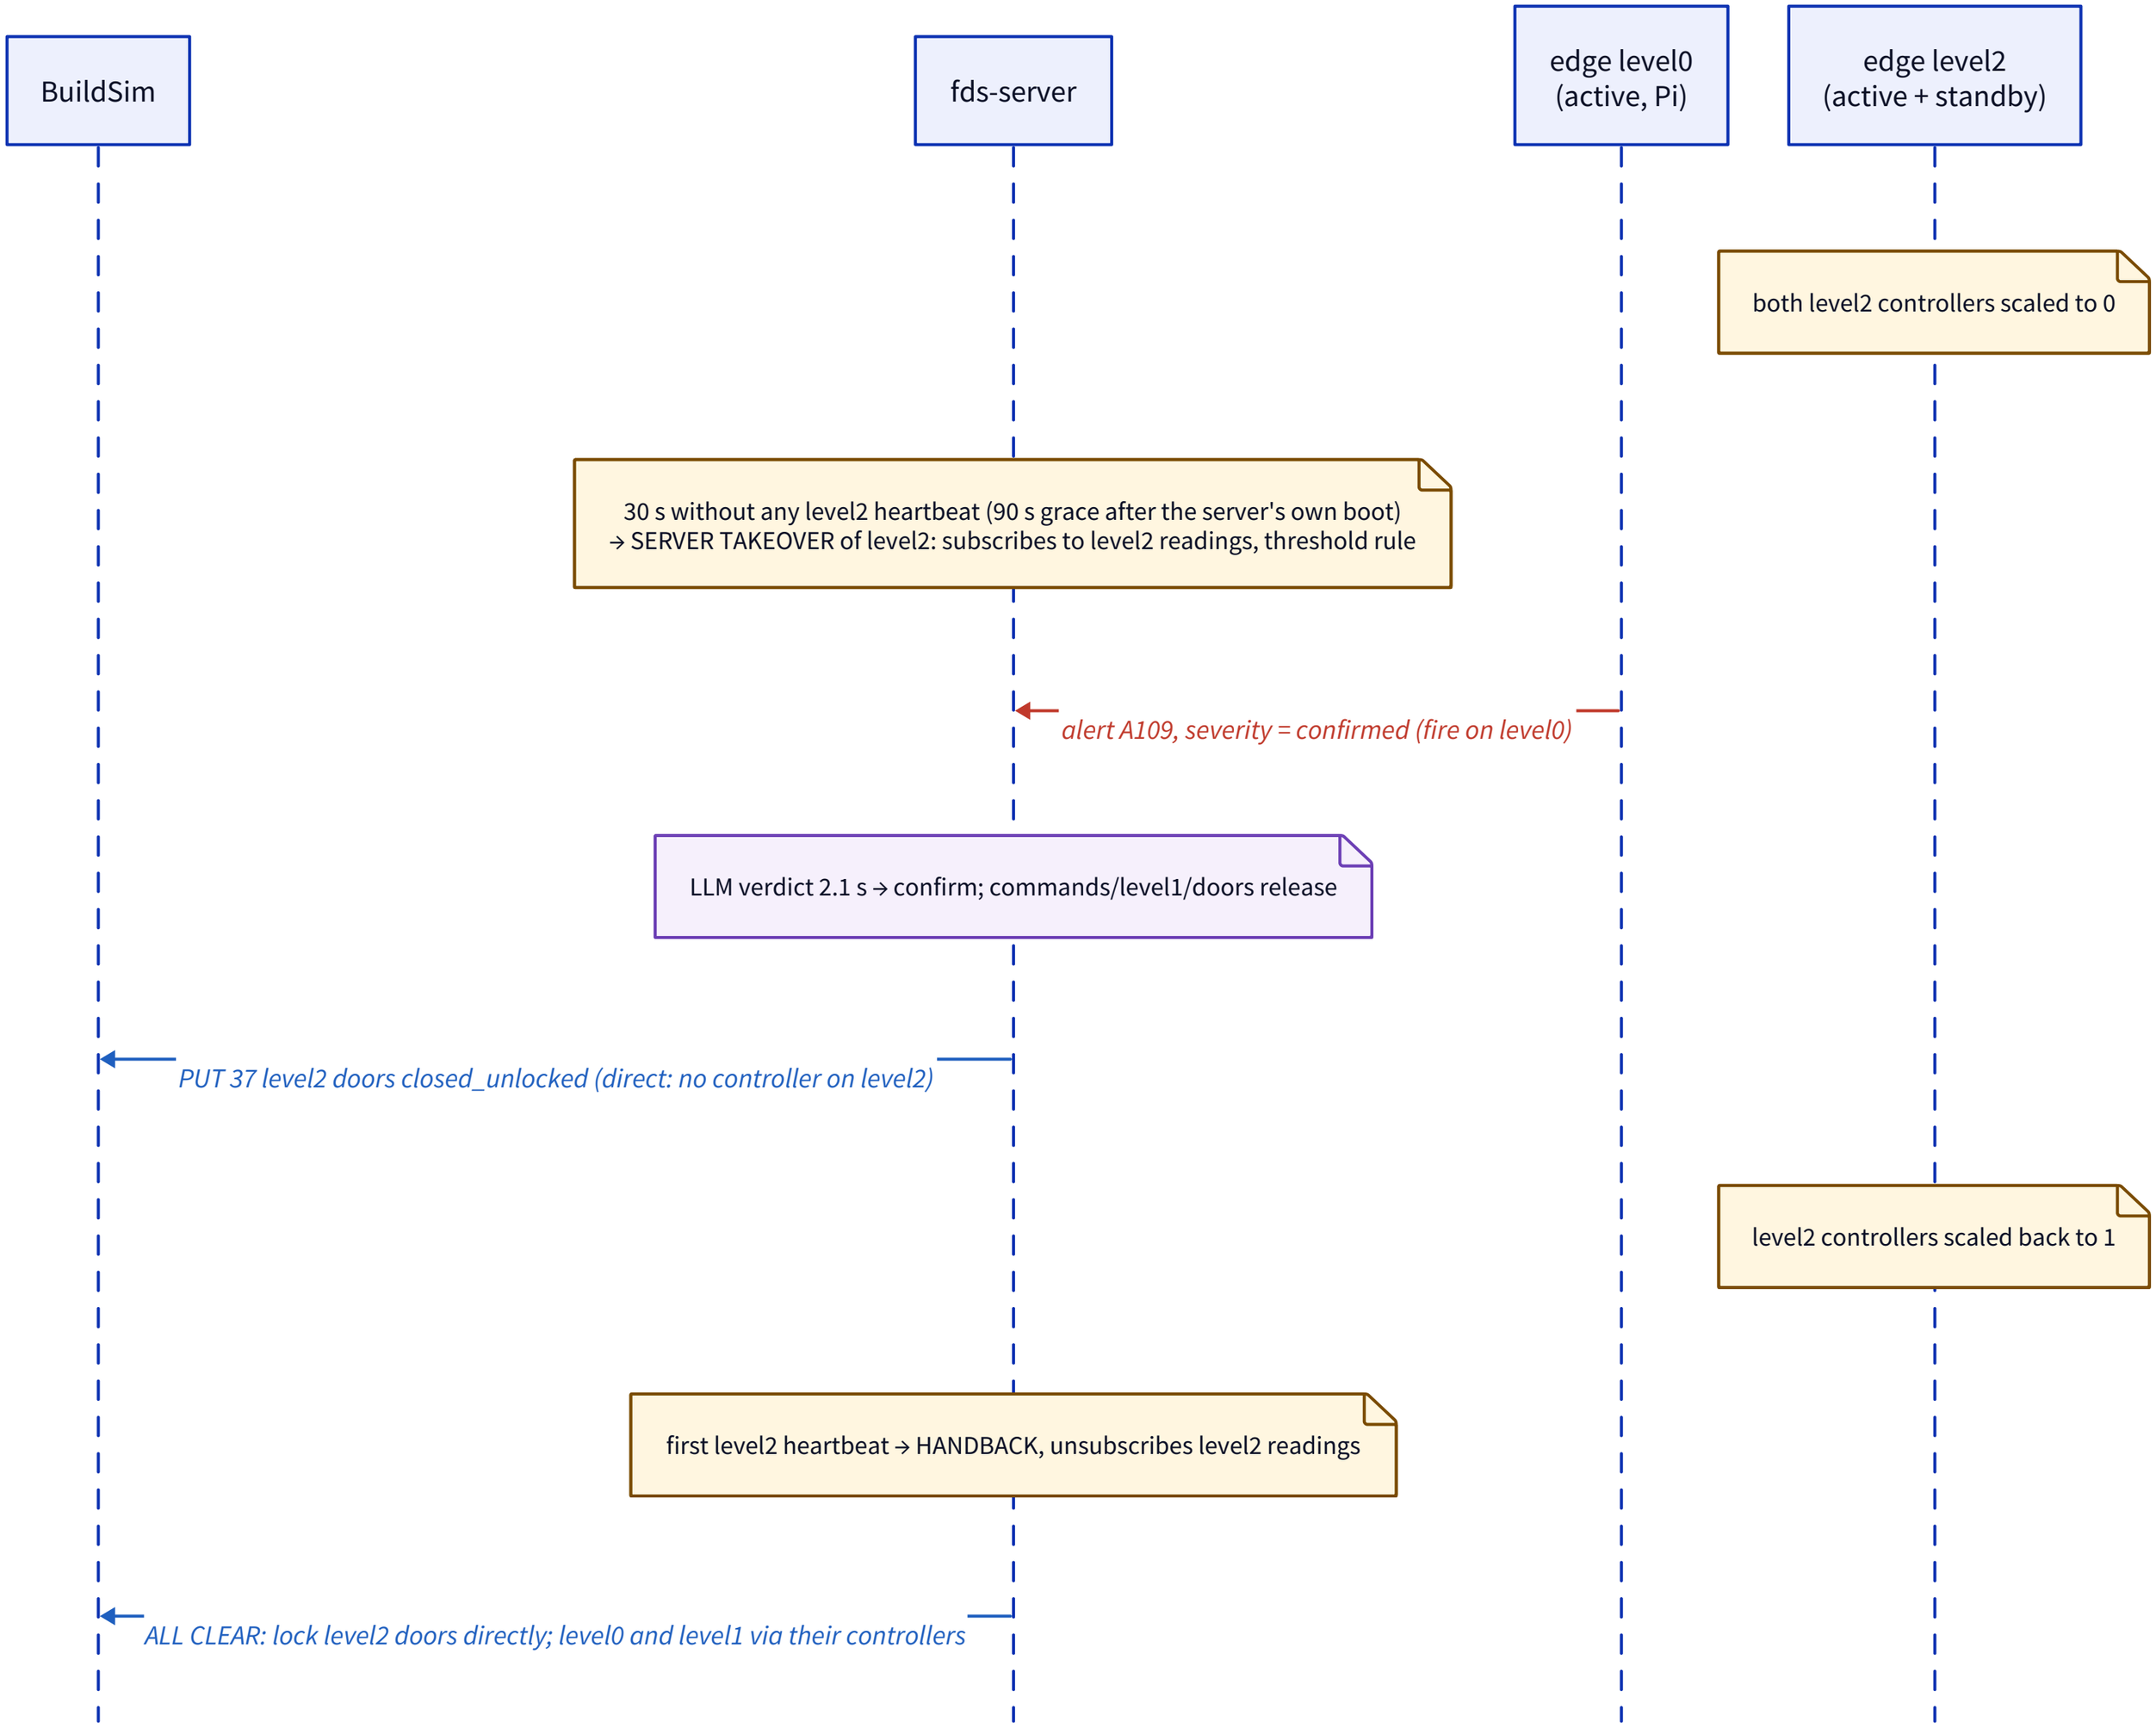

BuildSim
fds-server
edge level0
(active, Pi)
edge level2
(active + standby)
both level2 controllers scaled to 0
30 s without any level2 heartbeat (90 s grace after the server's own boot)
→ SERVER TAKEOVER of level2: subscribes to level2 readings, threshold rule
alert A109, severity = confirmed (fire on level0)
LLM verdict 2.1 s → confirm; commands/level1/doors release
PUT 37 level2 doors closed_unlocked (direct: no controller on level2)
level2 controllers scaled back to 1
first level2 heartbeat → HANDBACK, unsubscribes level2 readings
ALL CLEAR: lock level2 doors directly; level0 and level1 via their controllers
